

5,953

TOTAL TARGET WORKS

All target works

3,107

TOTAL COMPLETED

✓ Compl: 829

✓✓ Phys: 2,278

2,911

ABHIYAN PROGRESS

AFTER 19-MAR

✓ Compl: 633

✓✓ Phys: 2,278

₹154.30 Cr

TOTAL SANCTIONED

W: ₹102.55 Cr

M: ₹51.75 Cr

₹79.64 Cr

TOTAL BOOKED

(51.6%)

W: ₹58.18 Cr

M: ₹21.46 Cr

Work Type Progress

Snapshot 2026-06-06 · Model A max 9.0 / Model B max 10.0

All

9 work types

Jal Ganga 2025 Works

2 work types

Completion of Old MGNREGA Works

4 work types

New Works Taken-Up Jal Ganga 2026

1 work types

Farm Pond

A Model A · max 9.0

1,269

Completed + Phys.Compl.

Work Completion60.4%

Booked Expenditure55.8%

STARTED2,100

ONGOING831

SANCTIONED₹45.14 Cr

BOOKED₹25.20 Cr

Amrit Sarowar

A Model A · max 9.0

0

Completed + Phys.Compl.

Work Completion0.0%

Booked Expenditure23.1%

STARTED12

ONGOING12

SANCTIONED₹3.66 Cr

BOOKED₹0.85 Cr

Dug Well Recharge

A Model A · max 9.0

997

Completed + Phys.Compl.

Work Completion87.4%

Booked Expenditure80.8%

STARTED1,141

ONGOING144

SANCTIONED₹2.54 Cr

BOOKED₹2.05 Cr

Irrigation infrastructure

A Model A · max 9.0

21

Completed + Phys.Compl.

Work Completion80.8%

Booked Expenditure69.2%

STARTED26

ONGOING5

SANCTIONED₹0.55 Cr

BOOKED₹0.38 Cr

Water conservation & recharge

A Model A · max 9.0

516

Completed + Phys.Compl.

Work Completion78.2%

Booked Expenditure78.4%

STARTED660

ONGOING144

SANCTIONED₹36.17 Cr

BOOKED₹28.34 Cr

Watershed Related Works

A Model A · max 9.0

118

Completed + Phys.Compl.

Work Completion82.5%


Booked Expenditure76.5%

STARTED143

ONGOING25

SANCTIONED₹4.74 Cr

BOOKED₹3.63 Cr

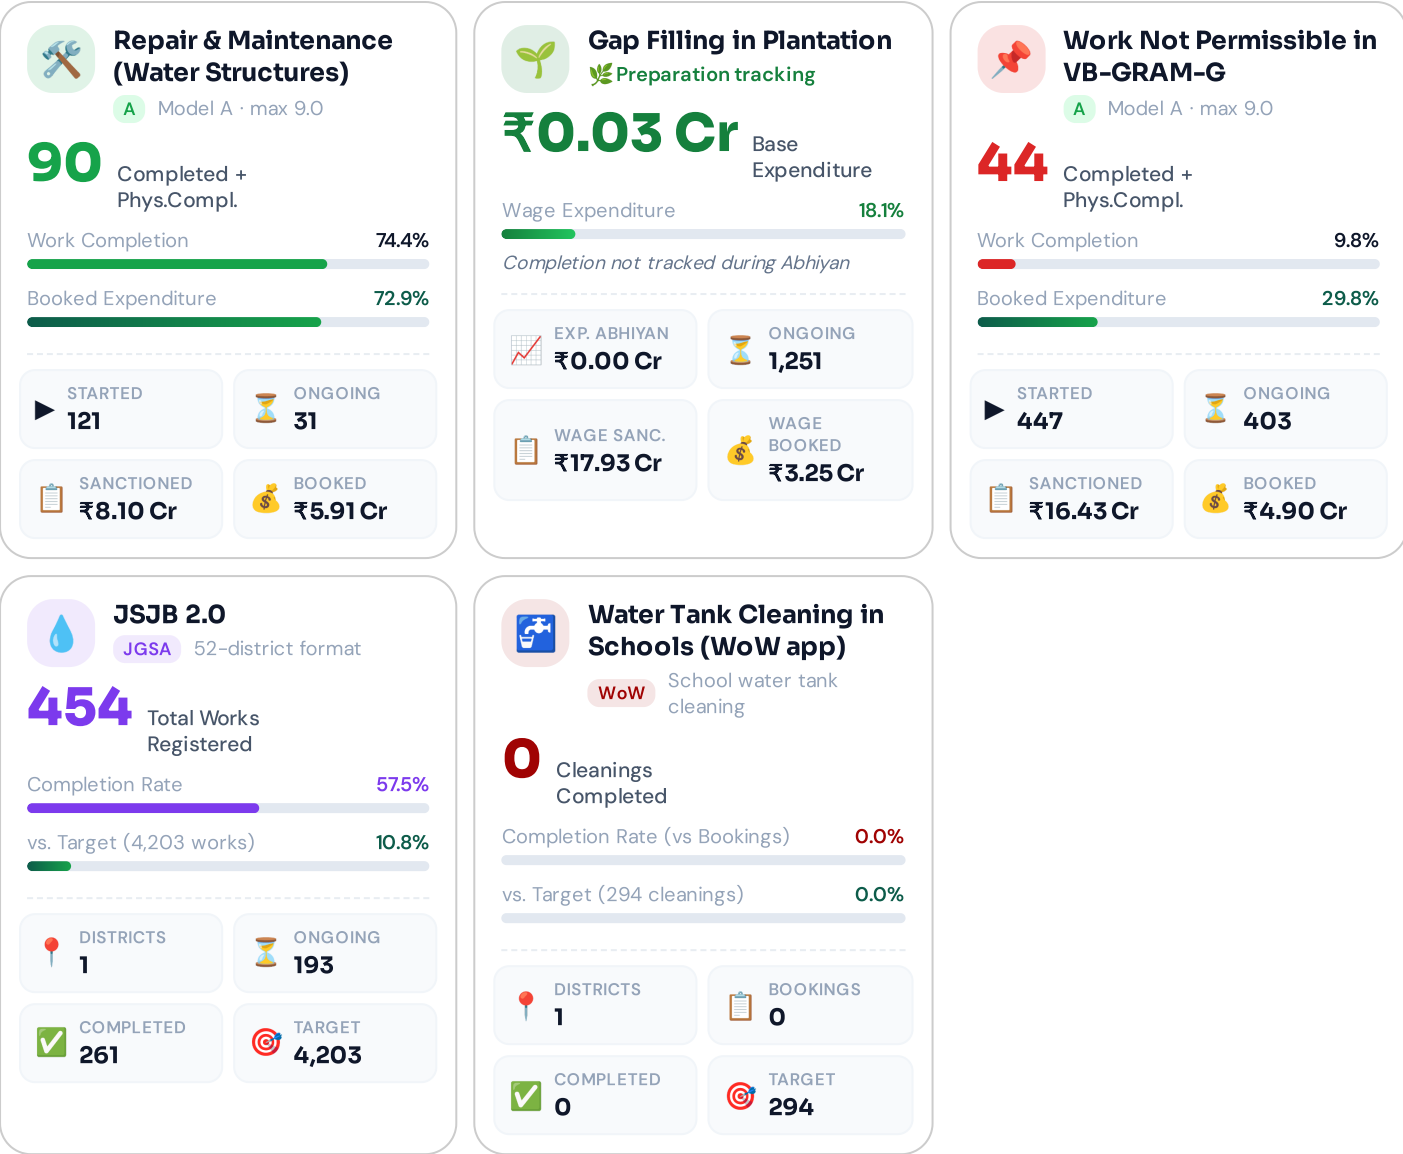

 Total Visits: **837,568** |  Today: **7,785** |  Unique Visitors (30 days): **107,873**
